


## Commissioning checklist

For full details refer to the installation instructions


### Installer, have you checked:

- Gas line and water pipes flushed of foreign matter before connection?
- Gas line connected and purged of air?
- Plumbing connections as shown, are correct?
- Final connection test completed?
- Supply pressures checked with all appliances operating?
- PCB settings checked if factory default temperature has been changed?
- System tested for gas leaks?
- Hot water delivery temperatures at all outlets checked?
- Do the controllers, if fitted, operate correctly?
- Cold water inlet filter inspected and cleaned?
- Tempering valve, if fitted, is suitable for continuous flow water heaters?
- Installation and flue clearances comply with AS/NZS 5601?
- Customer handover completed as per the installation instructions, checklist completed, signed and left for the homeowner.

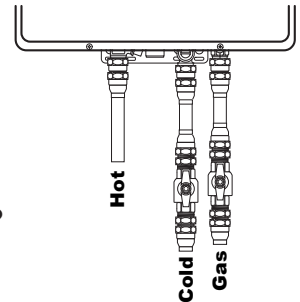

### For EF26 / A-Series models only with a sideways flue diverter fitted

- SW1 and SW3 of DipSW set to the ON position if a sideways flue diverter is fitted?



### For EF / N-Series models

- Have you connected a condensate drain pipe in accordance with the installation instructions?

### For internal models only

- Have you only used Rinnai flueing components?

Signed: \_\_\_\_\_

Date: \_\_\_\_\_

**N.B:** The warranty may be voided and a service charge incurred as a result of Rinnai attending a problem related to installation.

